
TIDEMARK CIVIL

TECHNICAL PROPOSAL / DEMONSTRATION RFP RC-27-01

NEW YORK CITY RESILIENT CORRIDORS INITIATIVE

Public infrastructure modernization,
flood resilience & pedestrian safety improvements

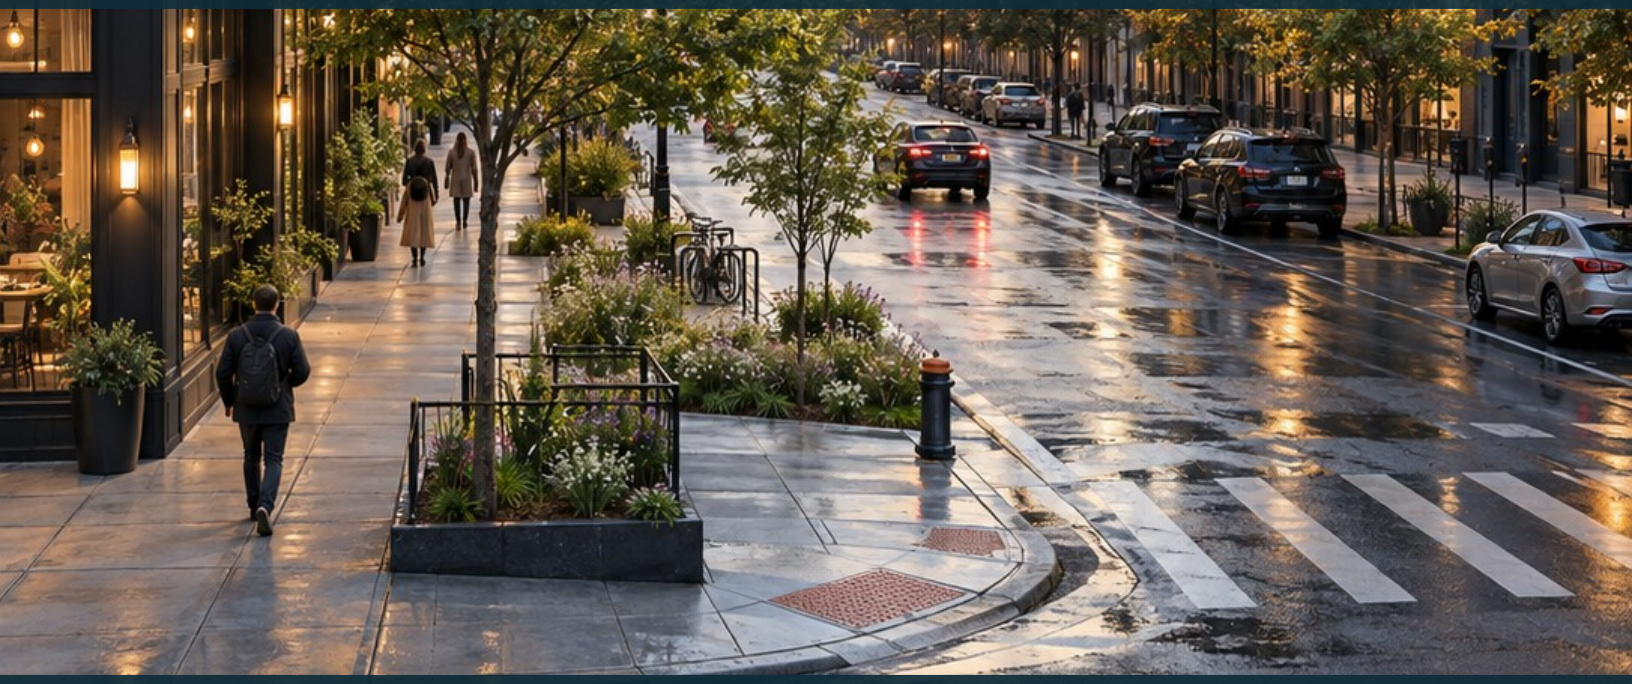

HARBOR REACH CORRIDOR

Fictional Brooklyn demonstration district
Prepared by Michael Ngo / November 2026

Independent proposal-development portfolio sample. Fictional project, contractor, and illustrative information. Prepared for professional demonstration purposes.

A more resilient street. A controlled path to delivery.

THE OWNER'S CHALLENGE

Harbor Reach must remain a working neighborhood while its infrastructure changes. Recurring rainfall ponding, constrained sidewalks and uncertain utility records create linked construction risks. Resolving drainage at the expense of access would leave the owner with a different problem.

Tidemark Civil proposes a block-by-block reconstruction strategy that verifies subsurface conditions before production excavation and carries each work area through documented acceptance. Drainage improvements, accessible corners and pavement restoration share one coordinated work plan.

The owner retains design authority and approval of scope changes. Our delivery team would identify conflicts early, present the schedule and cost implications, and obtain direction before affected work proceeds. This makes uncertainty visible while preserving a usable public corridor.

01

ACCESS THROUGH EVERY PHASE

A verified temporary route and entrance plan before each work zone opens.

02

VERIFIED CONDITIONS BEFORE PRODUCTION

Utility test pits and conflict decisions tied to the construction release.

03

ACCEPTANCE BEFORE REOPENING

Inspection records and a joint walk-through before the next block advances.

WHAT THE OWNER CAN VERIFY

A rolling six-week look-ahead links utility releases, public notices and inspection hold points. Weekly exception reporting identifies decisions needed, the accountable role and the effect on the next work area. Closeout records develop during construction so turnover does not become a separate recovery effort.

Proposed methods and commitments are illustrative. Performance would depend on the final contract, approved design, permits and verified site conditions.

Six blocks. One connected public corridor.


Assumed storefronts, crossings and utility interfaces guide the sequence of construction.

1,800 LF
illustrative corridor length

6 BLOCKS
three delivery reaches

18 MONTHS
from notice to proceed

CONCEPTUAL CORRIDOR PLAN / NOT A GEOGRAPHIC MAP

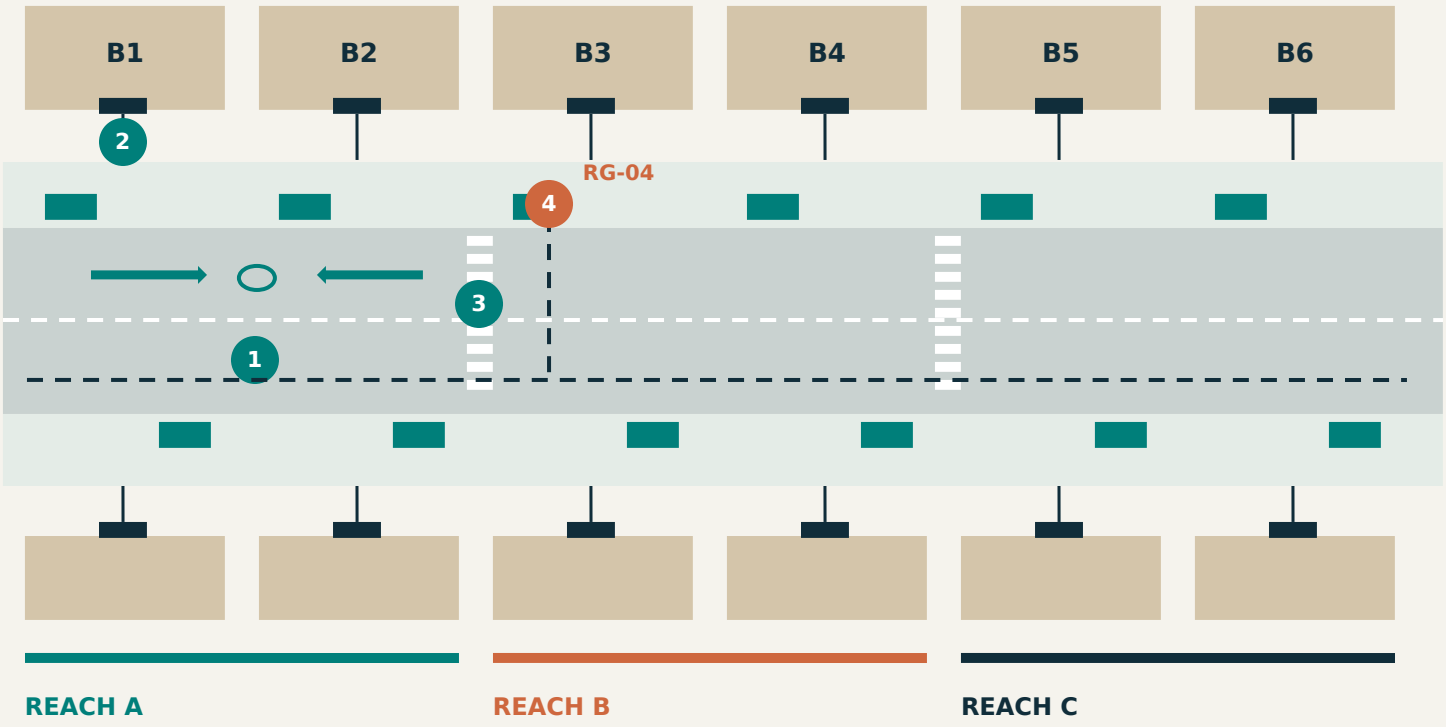

Green: candidate rain gardens Dashed navy: assumed utility White stripes: crossings

1 / DRAINAGE LOW POINT

Confirm grades, catchment and receiving drainage.

2 / STOREFRONT ENTRANCE

Maintain a signed route and agreed delivery access.

3 / CROSSING

Carry the public route through each construction phase.

4 / UTILITY INTERFACE


Test pit before RG-04 excavation. Worked example: page 11.

All frontages, low points and utility alignments are assumed. Final siting, capacity and clearances require investigation and the owner's approved design.

Drainage and accessibility share the same geometry.

Inlet placement, material acceptance and utility protection control each installation.

CONCEPTUAL SECTION / NOT TO SCALE

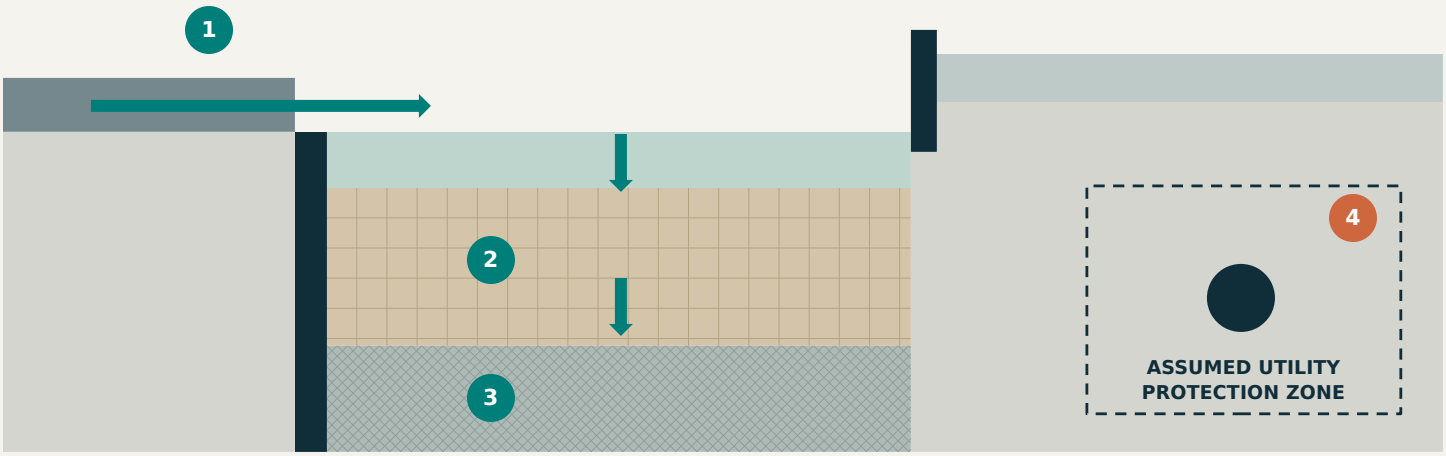

1 Curb opening

Runoff enters from the gutter.

2 Engineered media

Check approved mix and placement.

3 Stone reservoir

Drainage mode follows final design.

4 Utility interface

Verify location and required clearance.

GUTTER BYPASS / PLAN INSET

Downstream catch basin

Excess runoff continues along the gutter. Overflow routing requires the approved design.

Verify before excavation

Survey grades and test pit critical services. Resolve the utility interface before releasing the bed location.

Inspect before concealment


Record material acceptance, elevations and required tests before backfill. Protect new beds from sediment.

Concept only. The owner’s designer sets geometry, hydraulic capacity, media, infiltration or underdrain details, and utility protection. The inset represents a separate plan view.

Public access is a condition of each construction release.

A block advances only when the next temporary route is safe, legible and approved.

TYPICAL ACTIVE BLOCK / PLAN VIEW

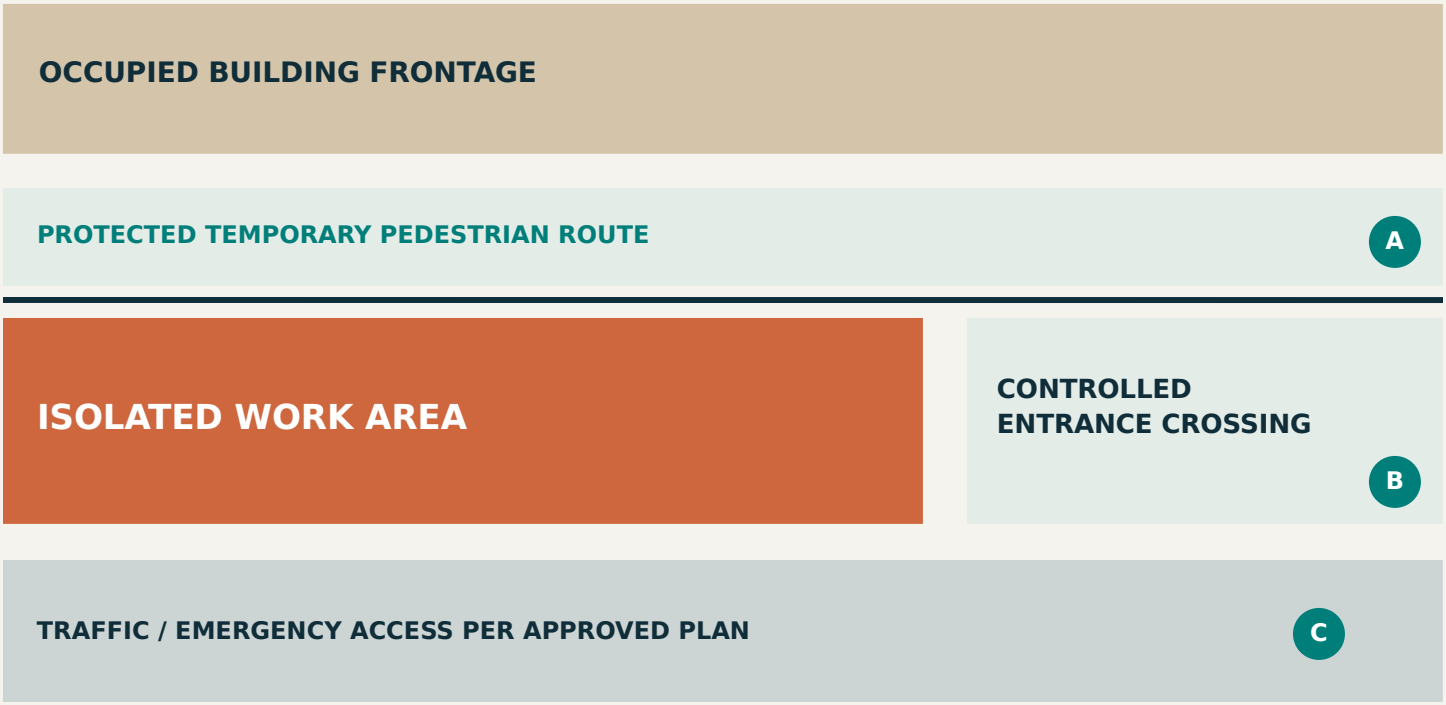

A / CONTINUOUS ROUTE

The superintendent and safety lead inspect barriers, surfaces, lighting and wayfinding before each shift and after any change. The approved plan governs clearances and crossing provisions.

B / ENTRANCES & DELIVERIES

The community liaison confirms affected entrances and delivery windows before notices issue. Temporary crossings require a designed, secured installation appropriate to the opening and expected use.


C / TRUCKS & EMERGENCIES

A designated spotter controls vehicle movements across pedestrian routes. Staging limits, emergency access and any lane closure require agency approval before mobilization.

Illustrative logistics diagram. Pedestrian routing, temporary works and traffic controls require site-specific review and approval. Construction never relies on public entry into an unprotected work area.

Interim reopening and final acceptance are distinct.

Illustrative 18-month baseline: April of Year 1 through September of Year 2.

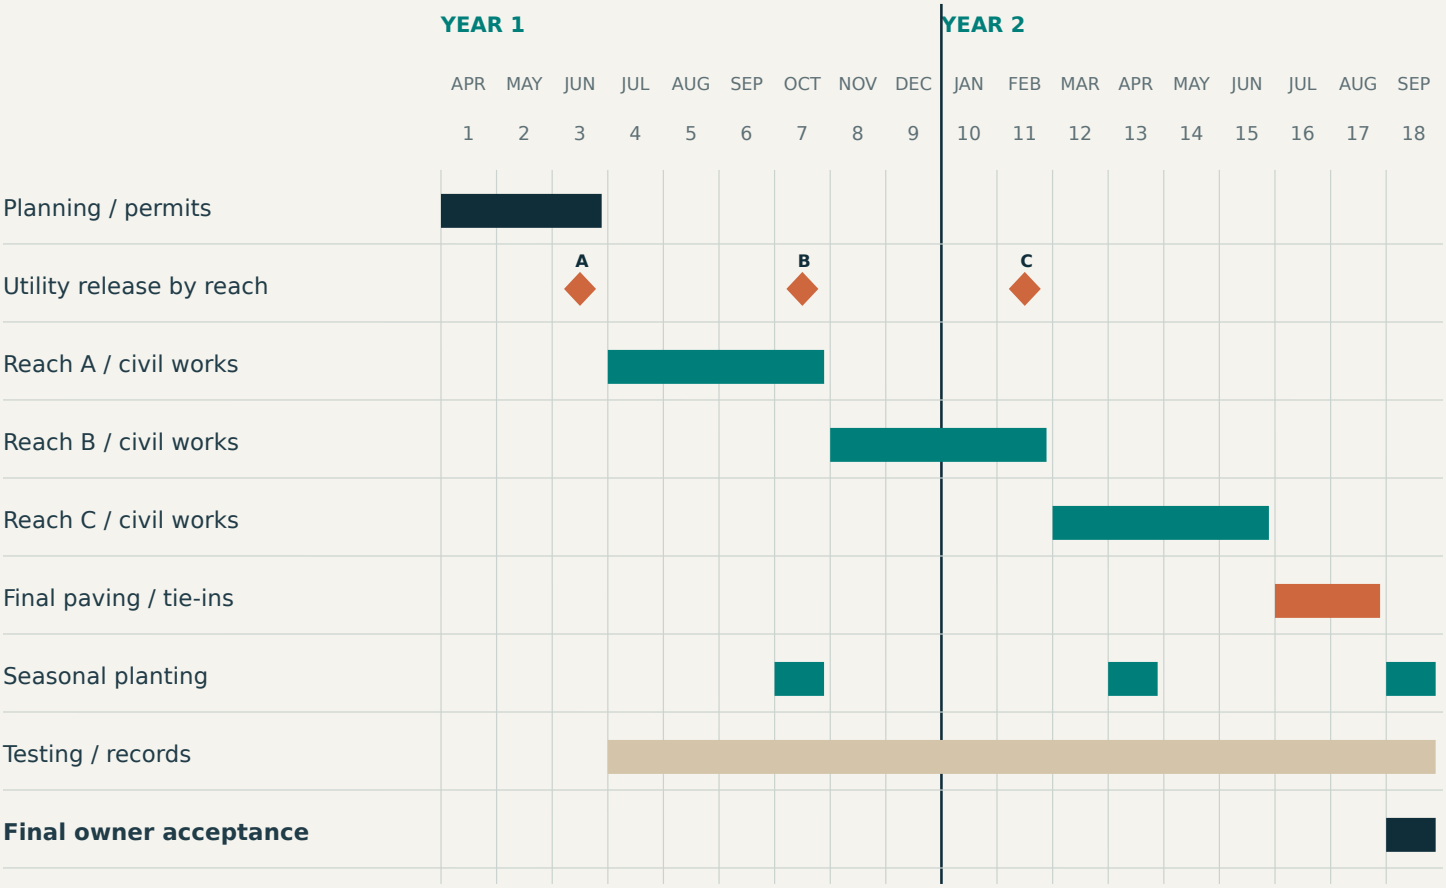

Diamond: utility release Teal: reach work / planting Orange bar: final paving

INTERIM REOPENING **A / M7 (OCT)** **B / M11 (FEB)** **C / M15 (JUN)**

Reopening gate

Confirm safe temporary or permanent surfaces, functioning drainage and accepted public routes before reopening a block. Reopening does not equal final owner acceptance.

Final completion gate

Complete corridor paving in M16–17. Plant in approved fall / spring windows, including M18. Close tests, punch items and turnover records before final acceptance in M18.

Each reach release requires permits, materials and resolved utility interfaces. Winter work assumes approved cold-weather protection. Delayed releases or unsuitable weather require resequencing.

Risk decisions belong in the daily work plan.

The superintendent owns field controls. Every worker may stop work when conditions become unsafe.

PRIORITIZED RISK REGISTER

Risk / trigger	Before	Proposed control / accountable role	After
Unknown utility Unverified service in excavation	3 × 3 9 / High	Test pits and utility release before production. Utility coordinator	1 × 3 3 / Med.
Pedestrian exposure Route or barrier changes	3 × 3 9 / High	Separate public route and daily inspection. Superintendent / safety lead	1 × 3 3 / Med.
Heavy rain Forecast or rising site water	2 × 3 6 / High	Secure excavation, protect inlets and suspend affected work. Superintendent	1 × 3 3 / Med.
Unsuitable soil Odor, staining or failed test	2 × 2 4 / Med.	Isolate, notify owner and follow approved characterization plan. Environmental lead	1 × 2 2 / Low
Approval delay Release date missed	2 × 2 4 / Med.	Track decision dates and resequence only released work. Project manager	1 × 2 2 / Low

Illustrative qualitative scores: likelihood 1–3 × consequence 1–3. Low 1–2, medium 3–4, high 6–9. “After” assumes controls are implemented and verified. Reassess whenever conditions change.

DAILY CONTROL CYCLE

1

PLAN

Task hazard review and weather check

2

VERIFY

Inspect barriers, utilities and access

3

AUTHORIZE

Confirm permits and release to work

4

REASSESS

Stop and revise when conditions change

Every concealed asset needs a visible record.

Inspection and test plans connect field acceptance to the owner’s turnover requirements.

01

PLAN THE EVIDENCE

The quality manager develops inspection and test plans from the approved drawings and specifications. Each plan names the inspection, acceptance criterion and required record.

02

VERIFY THE FIRST INSTALLATION

Review the initial drainage assembly, concrete placement and stormwater bed with the owner’s representative before repeating the work across the corridor.

03

INSPECT BEFORE COVER

Request required inspections in advance. Record elevations, utility clearances and approved test results before backfill or concealment.

04

CLOSE THE RECORD

Index accepted records by block and asset. Reconcile redlines, operation information and punch items during construction.

HOLD POINTS

Before backfill

Surveyed drainage inverts, inspection sign-off and specified pipe testing.

Before concrete

Subgrade / forms, reinforcing where specified and embedded items.

Before reopening

Surface acceptance, ramp checks, clear drainage path and public-route inspection.

NONCONFORMING WORK

Identify and isolate the affected work. Obtain the approved disposition, complete corrective action and reinspect before release. The quality manager reports unresolved items to the project manager and owner.

People should know what changes before it changes.

One community liaison maintains the access register and closes the loop on reported impacts.

NOTICE SEQUENCE FOR EACH WORK AREA

14 DAYS

1

Confirm access needs and delivery windows

7 DAYS

2

Issue approved notice and route diagram

48 HOURS

3

Reconfirm changes with affected frontages

DAILY

4

Check access and record new issues

WHO NEEDS WHAT

PUBLIC OWNER	Weekly progress, decision log and look-ahead. Escalate unresolved access or safety impacts immediately.
UTILITIES / TRANSPORTATION	Coordinate outages, closures and inspection windows before notices. Confirm the controlling approval in the release log.
RESIDENTS / BUSINESSES	Provide the dates, entrance arrangements, delivery impacts and a contact route in accessible formats appropriate to the audience.
EMERGENCY SERVICES	Confirm approved routes and any material access change through the owner’s established coordination process.


ILLUSTRATIVE SERVICE TARGET

Acknowledge routine inquiries within one working day. Assign an owner and next update time. Route urgent hazards immediately to site supervision and the appropriate emergency response.

Notice intervals are proposed planning targets, subject to the contract and agency requirements. Log issues, actions and closure confirmation without publishing personal information.

Clear authority at each field decision.

Proposed roles connect field supervision, independent quality review and specialist support.

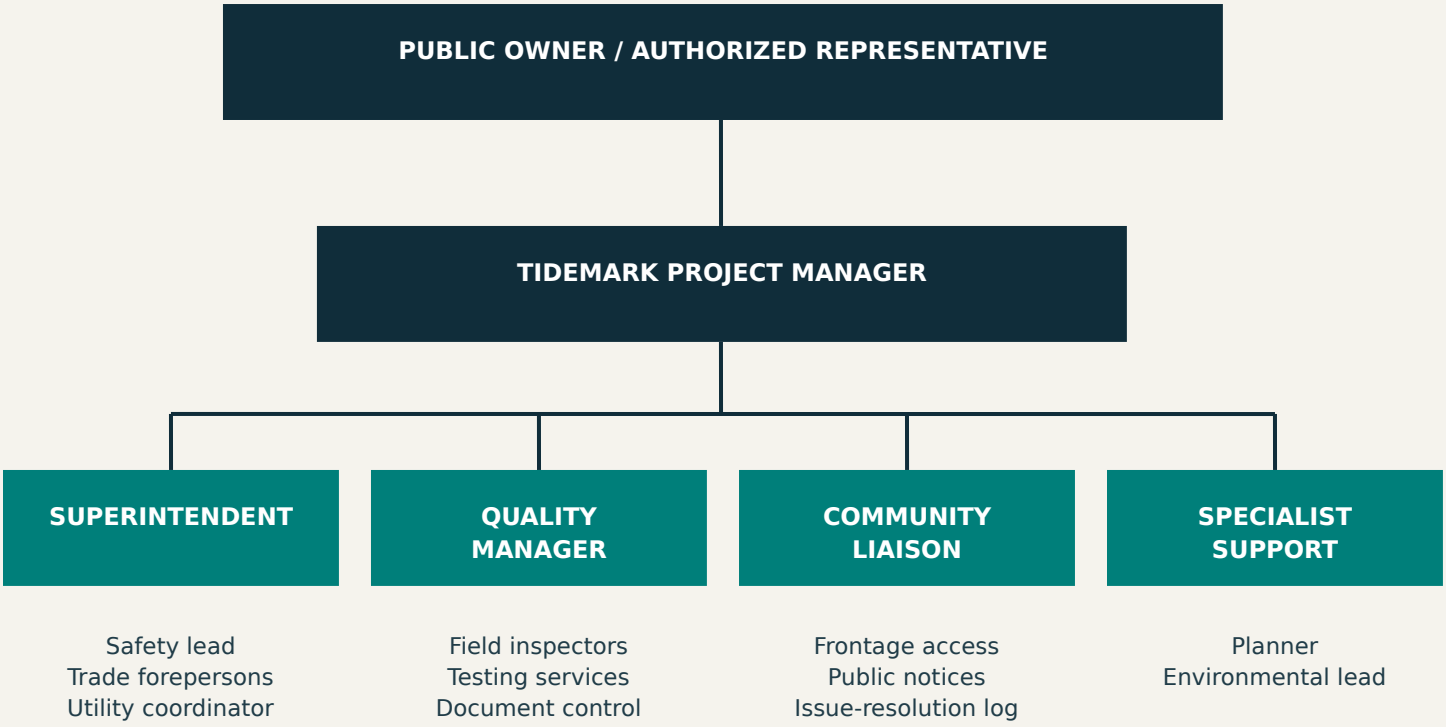

PROJECT MANAGER

Owns contractual notices and owner decisions. Integrates field, quality and specialist reports into cost and schedule control.

SUPERINTENDENT / QUALITY

The superintendent releases safe daily work. The quality manager can withhold acceptance of nonconforming work and escalates unresolved issues directly to leadership.

PLANNER / ENVIRONMENTAL LEAD

The planner tracks critical-path effects and reach releases. The environmental lead coordinates characterization, handling and disposal requirements when suspect material appears.

Roles are illustrative. The owner’s designer retains permanent-design authority. Utilities verify their services. Required qualified design and agency approvals remain conditions of release.


An unexpected service line. A controlled design decision.

Illustrative scenario: a test pit identifies an uncharted water service at candidate bed RG-04.

ASSUMED CONDITION / BLOCK 3


The discovered service crosses the proposed excavation envelope. The team holds affected work, protects the service and maintains the public route. Other released work can continue if safe and independent of the conflict.

ORIGINAL CANDIDATE LOCATION



Utility crosses candidate bed

ILLUSTRATIVE REVISED LOCATION



Designer verifies an alternate siting

Alternate siting is conditional on clearances, accessible space and hydraulic review. No field relocation proceeds without approved design and owner direction.

01 / RECORD	Utility coordinator captures the surveyed position, photographs and service-owner confirmation in an RFI.
02 / EVALUATE	The owner’s designer evaluates alternate siting and drainage performance. The planner assesses the reach-release effect.
03 / AUTHORIZE	The project manager submits cost / time effects and obtains written direction. The liaison updates affected frontage notices.
04 / RELEASE	Issue the revised drawing and work plan. Confirm utility protection and inspection requirements before excavation resumes.

Decision record: verified condition, RFI response, approved drawing, owner direction and inspection release. See Appendix A (pages 14 –20) for the workflow map, worked record and release checks.

A traceable response. A controlled scope.

Demonstration requirements below are authored for this fictional RFP, rather than copied from an actual solicitation.

Demo RFP requirement	Response / evidence	Accountable role
§ 2 / Project understanding	Defined assumptions and corridor plan Page 3	Project manager
§ 3 / Technical methodology	Approach, utility example and procedure Pages 4–5, 11 and Appendix A	Superintendent
§ 4 / Delivery schedule	18-month sequence and release logic Page 6	Planner
§ 5 / Safety and quality	Risk register and inspection hold points Pages 7–8	Safety / quality leads
§ 6 / Community and staffing	Notice sequence and role structure Pages 9–10	Liaison / project manager

Submission control

Maintain a single compliance register with the requirement, response location, owner and verification status. Record addenda, reconcile cross-references and confirm the final package against the submission instructions.

Cost and change control

Link field quantities to approved pay items and accepted records. Identify scope variance through a written notice with the cause, options and schedule effect. Obtain authorized direction before changed work proceeds.

BOUNDARIES OF THIS SAMPLE

This technical sample excludes a bid price, bonds, insurance evidence and executed forms. It assumes local rainfall-drainage improvements, with no coastal-surge barrier, major sewer replacement or unverified flood-protection capacity. Actual permits, labor requirements and participation goals would follow the issued contract.

A corridor ready for daily use. Records ready for the owner.

Proposed value is measured through accepted work and a usable public environment.



Conceptual streetscape. Not an existing project or an engineering detail.

RESILIENCE

Approved drainage assets with inspection evidence and clear maintenance access.

PUBLIC SAFETY

A verified route during construction and accepted pedestrian facilities at turnover.

DELIVERY CONTROL

Released work areas, visible decisions and a schedule tied to utility and inspection constraints.

TIDEMARK CIVIL

New York City Resilient Corridors Initiative
Technical proposal / November 2026

Utility conflict review and work release

TC-PRO-001 / Revision 1.0 / November 2026

Use this procedure to document a utility conflict, obtain the required decisions and verify readiness before affected work resumes. It governs the proposed information and approval workflow for Harbor Reach. It does not prescribe excavation methods or replace the approved site safety plan.

Document control

Field	Controlled value
Document and issue	TC-PRO-001 / Revision 1.0 / Initial portfolio issue
Status and audience	Fictional demonstration / utility coordinator, superintendent and project team
Related example	Block 3, candidate rain garden RG-04 / proposal page 11
Working rule	Use the contract-designated authority and current approved documents.

Responsibilities and records

Role	Responsibility in this procedure
Utility coordinator	Maintains the condition record and utility confirmation evidence.
Superintendent	Controls the affected work area and authorizes field resumption within delegated authority.
Project manager	Obtains contractual direction and records cost and time decisions.
Designer and utility owner	Provide design disposition and service confirmation within their respective authority.
Quality manager and support	Quality verifies inspection readiness. Planner checks sequencing. Liaison updates access notices.

Navigation: A2 Capture the condition. A3 Track status. A4 Read the end-to-end workflow. A5 Verify release. A6 Read the worked record. A7 Check acceptance scenarios and terms. All project data and proposed controls are illustrative.

Capture the field condition

Task 1 / Create a traceable record before requesting a decision

Start when a verified or suspected service conflicts with the current construction information. The superintendent controls the field response under the approved site plan. The coordinator documents the condition without entering an unsafe area or directing unauthorized service work.

1 Locate	Identify the block, asset and affected activity. Record the discovery point against the current drawing. State whether the alignment is observed, surveyed or inferred.
2 Attach evidence	Reference approved field photographs, the location sketch and relevant drawing revision. Label the evidence so a reviewer can connect each item to the condition.
3 Describe the difference	Separate the observed condition from assumptions. Identify any unconfirmed service type, owner, depth or operating status. Do not report an assumption as verified.
4 Request a decision	Issue a request for information (RFI) that names the conflict and the decision needed. Include the required response date from the look-ahead. Keep affected work on hold pending the required releases.

Minimum field record

Field	Required content	Illustrative example
Record ID	Unique reference and revision	RFI-UC-004 / Rev 0
Location	Block and asset identifier	Block 3 / RG-04
Baseline	Drawing number and revision	CR-C-103 / Rev 0
Condition	Observed conflict and uncertainty	Service crosses bed envelope; identity unconfirmed
Evidence	Distinct attachment references	PH-04A, PH-04B and SK-04 / Rev A

Task output: one condition record with evidence references, affected activity, responsible coordinator and a clear question. If a required field is unavailable, record it as unconfirmed and assign the follow-up.

Track review status and work readiness

Task 2 / Keep design review and permission to resume as separate decisions

Track review status and work status separately. Review may advance while work remains BLOCKED. A state changes only when its entry evidence is present and the responsible role records the transition. An RFI response alone does not authorize field resumption.

Track and state	Entry evidence or condition	Record owner
Review / OPEN	Condition record and attachments logged. Affected work identified.	Utility coordinator
Review / IN REVIEW	Designer and utility reviewers have the current record and the question requiring disposition.	Project manager
Review / DIRECTION RECEIVED	Required written owner direction identifies the accepted disposition and applicable drawing revision.	Project manager
Work / READY FOR RELEASE	Every applicable check on A4 passes. The field team has not yet authorized resumption.	Quality manager
Work / RELEASED	Superintendent records the permitted scope and confirms the required quality release.	Superintendent
Work / BLOCKED	A required decision, record or check is missing, or a changed condition invalidates prior evidence.	Role identifying the gap

Exceptions and escalation


When information is incomplete, identify the missing item, assign its owner and record the next review date. The planner evaluates whether the pending decision affects the reach-release milestone. Re-sequence only work that is safe, authorized and independent of the conflict.

For this workflow, BLOCKED describes work readiness, not the progress of design review. A verbal instruction, unanswered RFI or unapproved sketch does not satisfy written direction. Follow the issued contract if its authority or records differ.

Utility conflict decision and release workflow

End-to-end control map / Follow the arrows; records named below are the evidence for each transition

Use this map after a suspected or verified conflict is identified. The lanes show responsibility; the decision gates show why technical review, contractual direction and field release remain separate. A No result routes the affected work to BLOCKED until the missing evidence is resolved.

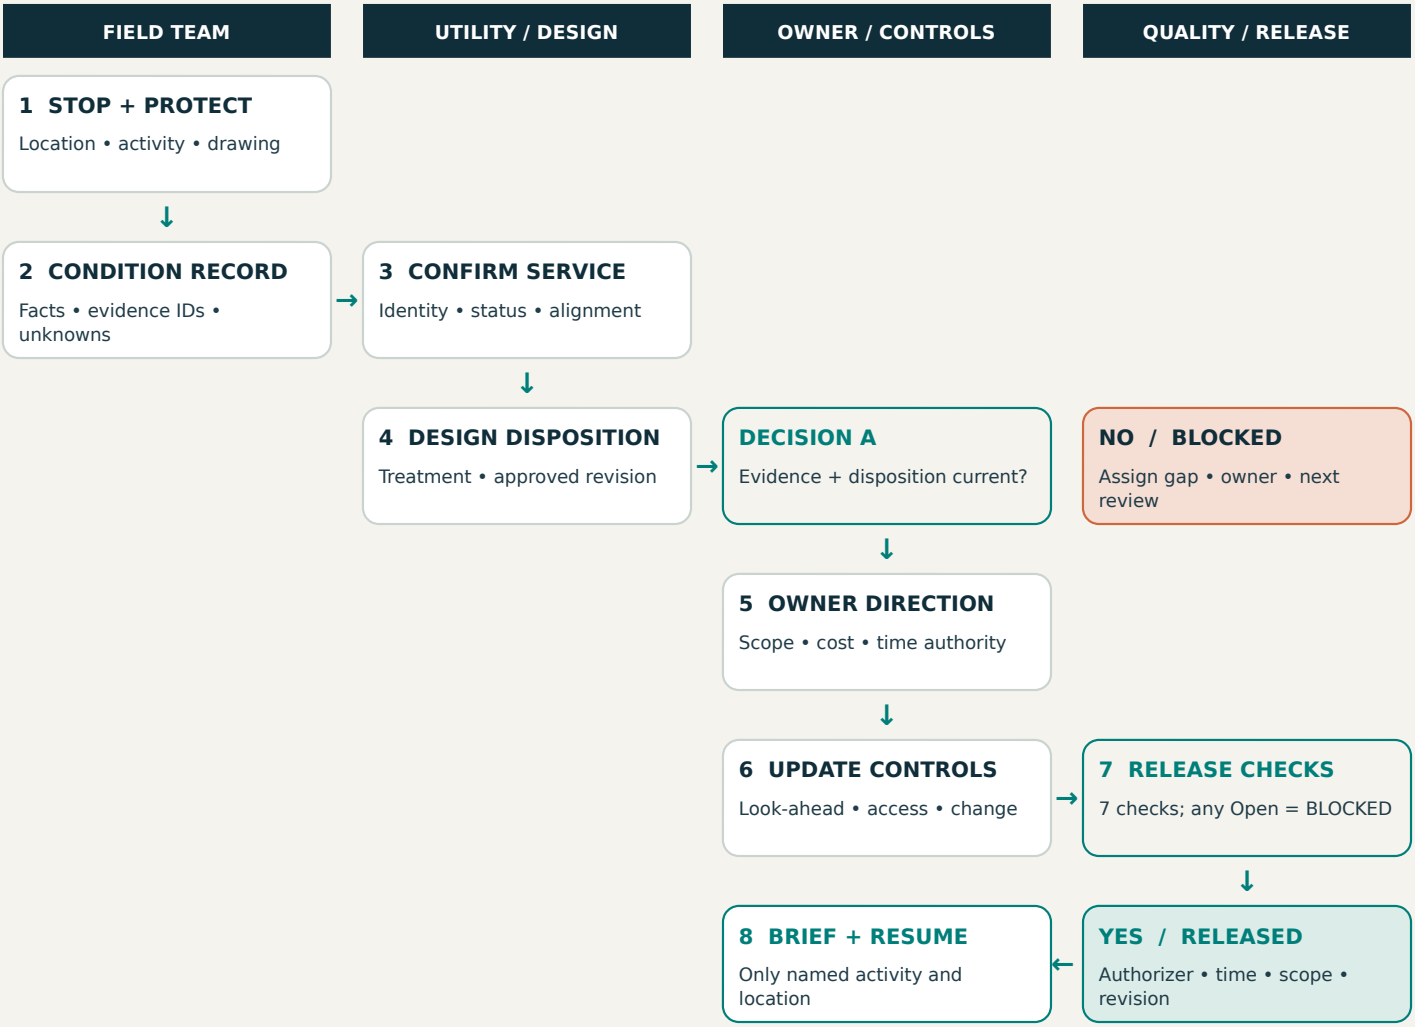

Changed condition or revision → invalidate release → return to Step 1

Control rule: a design response can advance review without releasing work. Only the defined activity, location and drawing revision named in the completed release record may resume. A changed condition returns the process to field capture.

Verify readiness and release affected work

Task 3 / Record each check as Pass, Open or Not applicable with an accepted reason

Use the checklist for the specific asset and work area. Any Open item keeps affected work BLOCKED. A Not applicable entry needs a documented reason accepted by the designated reviewer. An empty field does not count as a pass.

Check	Evidence to verify	Pass condition
Location and revision	Condition record and approved drawing	Asset and location match the current revision.
Utility interface	Service-owner confirmation and design disposition	Required identity, protection and clearances are resolved.
Owner direction	Written instruction and change record	Required scope, cost and time direction is recorded.
Public access	Current route plan and affected-frontage notices	Approved arrangements apply to the planned work period.
Work plan and safety	Applicable permits and approved site controls	Superintendent confirms conditions for the authorized task.
Inspection readiness	Inspection and test plan and required bookings	Hold points, notice requirements and records are assigned.
Release record	Completed checklist and role confirmations	Superintendent and quality release the defined scope.

1 Confirm

Quality records the checklist result and the evidence revisions. Superintendent confirms that actual conditions match the reviewed work plan.

2 Release

Record who authorized resumption, when, for which location and activity, and under which drawing revision. Communicate the release to affected crews.

Invalidate and recheck the release if the service position, design revision, public route, permit condition or work method changes. Work release permits the defined activity. It does not constitute final owner acceptance of completed construction.

Worked RFI and status record

RFI-UC-004 / All identifiers and entries below are fictional

This completed example demonstrates how to record an unresolved condition without implying approval. It extends the RG-04 scenario in proposal page 11.

Field	Illustrative entry
Discovery and location	Month 5, week 2 / Block 3 / candidate bed RG-04
Baseline document	CR-C-103 / Rev 0 / proposed bed excavation envelope
Observed condition	A service line crosses the proposed envelope. Service identity and operating status remain unconfirmed.
Evidence references	PH-04A and PH-04B / SK-04 Rev A. Survey confirmation remains open.
Decision requested	Confirm the service and issue an approved disposition preserving required clearances, accessible space and drainage function.
Proposed response	Consider shifting the bed along the curb zone. Hydraulic and utility review remain required.
Authority and impacts	Written owner direction not received. Planner is checking the Reach B release window.
Assigned follow-up	Coordinator obtains utility confirmation. Project manager obtains the design response and required direction.

Current work status BLOCKED

Review status is IN REVIEW. Work status is BLOCKED. Utility and survey confirmation, approved design disposition and written owner direction remain open. A5 cannot pass until these items are resolved and the remaining release checks are complete.

Recommended next update: next project coordination review, or earlier if the reach-release date is threatened. Keep the current location and revision on every attachment. No completed approval, signature or real project performance is represented.

Acceptance scenarios and reference terms

Use these scenarios to check the documentation logic before adopting or revising the procedure

Scenario	Expected result	Reason
Design response only	BLOCKED	Contractual direction and field checks remain separate.
Drawing revision mismatch	BLOCKED	Evidence does not match the proposed work.
All checks pass, no field release	READY FOR RELEASE	The authorized field transition is still pending.
Authorized scope and release recorded	RELEASED	All required gates and role confirmations are complete.
New condition after release	BLOCKED and reassess	The earlier evidence may no longer support the work.

Reference terms

Term	Meaning in this appendix
RFI	A request seeking clarification or a documented design response.
Hold point	A checkpoint requiring the specified inspection or permission before proceeding.
Current approved revision	The design issue authorized for the activity and named in its release record.
Work release	Permission to resume a defined activity after the required checks.
Interim reopening	A safe public route reopened before all permanent work is complete.
Final owner acceptance	Contract-defined acceptance of finished work and required turnover records.

Revision and verification

Review this procedure when contract authority, the approval sequence or the record system changes. Issue a superseding revision, withdraw obsolete copies and brief affected users. The scenarios above are expected outcomes, not a claim that a real system or field process has been tested.

Background: the fictional Harbor Reach proposal and its authored solicitation brief. General stormwater context: NYC DEP, Green Infrastructure on Streets and Sidewalks. This appendix defines an illustrative records workflow, not an engineered construction method.
